

HiLCoE School of Computer Science & Technology

Department of Software Engineering

GROUP PROJECT REPORT

Applying the Five Project Management Process Groups 4-Module MVP Scope

Retail & Local E-Commerce

A hyper-local online marketplace for small and medium retail shops

Proposed product name: "AddisSuq"

Course title	Software Project Management
Course code	SE341
Group	Group 3
Project title	Retail & Local E-Commerce (MVP scope: 4 modules)
Project manager	Yared Mengiste (ZP9157)
Project duration	6 weeks Mon 20 Jul to Fri 28 Aug 2026 (30 working days)
MVP modules built	(1) Vendor Onboarding & Product Catalogue · (2) Customer Accounts, Location & Discovery · (3) Cart, Checkout & Payment · (4) Delivery, Order Tracking & Notifications
Estimated budget	ETB 225,000
Submitted to	Mr. Hassen Redwan, Course Instructor
Submission date	August 30, 2026

Group Members

No.	Full name	Student ID	Project role
1	Abenezer Yohannes	PJ4151	Requirements / Business Analyst
2	Nathnael Mesfin	OT8453	Technical Lead / Backend Developer
3	Osama Sufiyan	YT1430	Backend Developer
4	Saron Edosa	ZZ9284	UI/UX Designer
5	Yared Mengiste	ZP9157	Project Manager (Team Leader)
6	Yasser Abdulhafiz	KE2168	Frontend Developer
7	Yamlak Abnet	AI0828	Frontend Developer / Documentation Officer
8	Zikra Seid	BB1717	QA / Test Engineer & Risk Officer

1. Introduction and Project Overview.....	3
1.1 Course and group information.....	3
1.2 Product concept, business need and MVP scope.....	3
1.3 Roles and responsibilities of team members.....	3
1.4 Communication among team members.....	4
2. Project Management Approach.....	5
How the process groups map onto the six weeks.....	5
3. Business Case.....	5
3.1 Introduction / background.....	5
3.2 Business objective.....	6
3.3 Current situation and problem / opportunity statement.....	6
3.4 Critical assumptions and constraints.....	6
3.5 Analysis of options and recommendation.....	6
3.6 Preliminary project requirements (MVP).....	7
3.7 Budget estimate and financial analysis.....	7
3.8 Schedule estimate.....	7
3.9 Potential risks.....	7
4. Project Charter.....	7
5. Team Charter.....	9
6. Project Scope Statement.....	10
6.1 Project summary and justification.....	10
6.2 Scope boundaries.....	10
6.3 Product characteristics and requirements (4 MVP modules).....	11
6.4 Project-management-related deliverables.....	11
6.5 Product-related deliverables.....	12
6.6 Project success criteria.....	12
7. Work Breakdown Structure (WBS).....	13
7.1 WBS in outline form.....	13
7.2 WBS dictionary (selected work packages).....	14
8. Project Schedule and Gantt Chart.....	15
8.1 Task list with durations, dates and dependencies.....	15
8.2 Gantt chart.....	18
8.3 Critical path and schedule notes.....	21
9. List of Prioritised Risks.....	21
10. Milestone Report.....	23
11. Cost Baseline and Budget Detail.....	24
12. Conclusion.....	25
References.....	25

1. Introduction and Project Overview

1.1 Course and group information

Course name	Software Project Management
Course code	SE341
Instructor / Project sponsor	Mr. Hassen Redwan
Group	Group 3, eight members
Project title	Retail & Local E-Commerce 4-module MVP
SPM approach / model used	Hybrid: a predictive backbone organised around the five project management process groups, with the executing work delivered in two iterations of incremental delivery
Group members	Abenezer Yohannes (PJ4151), Nathnael Mesfin (OT8453), Osama Sufiyan (YT1430), Saron Edosa (ZZ9284), Yared Mengiste (ZP9157), Yasser Abdulhafiz (KE2168), Yamlak Abnet (AI0828), Zikra Seid (BB1717)

1.2 Product concept, business need and MVP scope

Most small and medium retail shops in Addis Ababa – clothing boutiques, electronics shops, cosmetics stores, stationery shops and mini-markets – still sell only to walk-in customers. They have no low-cost way to show what is in stock, and customers have no reliable way to find out which nearby shop has the item they want at what price. This project delivers AddisSuq, a web and mobile hyper-local marketplace that lets shops list products and lets nearby customers discover, order, pay for and receive them.

Following the class instruction to scope the six-week build to three or four implementable modules, the group selected four modules that together form one complete, demonstrable order-to-delivery flow – the minimum a customer needs to discover a shop, buy something and receive it, and the minimum a shop needs to sell:

- **Module A – Vendor Onboarding & Product Catalogue:** shop registration and approval, plus the product catalogue and inventory a shop needs to sell anything at all.
- **Module B – Customer Accounts, Location & Discovery:** customer sign-up and location capture, plus distance-based search and browsing, so a customer can find a shop's products.
- **Module C – Shopping Cart, Checkout & Payment:** cart, order placement and payment (Telebirr, CBE Birr, Chapa and cash on delivery), the step that turns browsing into a sale.
- **Module D – Delivery/Pickup, Order Tracking & Notifications:** delivery or pickup scheduling, order-status tracking and SMS/e-mail notification, which closes the loop from order to receipt.

Ratings and reviews, the vendor sales dashboard, and the full platform administration console are deliberately deferred beyond this six-week build (Section 6.2 lists them as out of scope for this project). They add polish and vendor-side reporting but are not required for a customer to complete a real, trackable purchase, which is what the sponsor's success criterion in Section 4 tests for.

"AddisSuq" is a proposed working name; the group may change it before launch.

1.3 Roles and responsibilities of team members

Each member holds one primary role for the whole project. With four modules instead of the original twelve product characteristics, each developer owns one module end to end (frontend and backend pairs share a module), which keeps handoffs to a minimum inside a short six-week build.

Name	ID	Role	Key responsibilities
Mr. Hassen Redwan		Project Sponsor / Client Representative	Approves the business case and project charter, reviews deliverables at each milestone, resolves escalated issues and gives the final acceptance sign-off.
Yared Mengiste	ZP9157	Project Manager (Team Leader)	Leads planning; owns the scope statement, WBS, schedule and cost baseline; chairs the daily stand-up

			and iteration meetings; consolidates weekly progress reports; runs change control; prepares the final project report.
Abenezer Yohannes	PJ4151	Requirements / Business Analyst	Prepares the business case; runs the customer survey and shop-owner interviews; writes the requirements specification; drafts the scope statement; defines acceptance criteria with the sponsor.
Nathnael Mesfin	OT8453	Technical Lead / Backend Developer (Module A + payments)	Defines the architecture, data model and API contracts; sets up environments and CI/CD; builds vendor onboarding and shop approval (Module A); integrates the payment gateways (Module C); performs production deployment.
Osama Sufiyan	YT1430	Backend Developer (Module A catalogue + Module C cart)	Builds the product catalogue, categories and inventory (Module A); builds the shopping cart and order placement (Module C); supports the cost estimate.
Saron Edosa	ZZ9284	UI/UX Designer	Produces wireframes, the style guide and the high-fidelity screens for all four modules; runs the usability review; prepares vendor training material, the user guide and the launch promotion package.
Yasser Abdulhafiz	KE2168	Frontend Developer (Module B accounts + Module D delivery)	Builds customer sign-up, log-in and location capture (Module B); builds the delivery and pickup scheduling screens (Module D).
Yamlak Abnet	AI0828	Frontend Developer / Documentation Officer (Module B search + Module D tracking)	Builds location-based search and browsing (Module B); builds order tracking and notifications (Module D); maintains the project and user documentation.
Zikra Seid	BB1717	QA / Test Engineer & Risk Officer	Writes the test plan and test cases; runs integration and regression testing across all four modules; maintains the defect log; coordinates user acceptance testing; owns the risk register.

1.4 Communication among team members

Because all eight members also carry other coursework, communication is kept short, written and predictable.

Communication	Purpose	Format/medium	Frequency	Participants	Owner
Daily stand-up	Report progress, plan for today, raise blockers	Face-to-face / Telegram voice call	Daily, 5:00 pm (15 min)	All members	Project Manager
Iteration planning meeting	Agree the scope of the next iteration and assign work	Face-to-face meeting	Start of each of the 2 iterations	All members	Project Manager
Iteration review & demo	Demonstrate the working increment and obtain acceptance	Live demonstration	End of each of the 2 iterations	All members + sponsor	Project Manager
Weekly progress report	Record work completed, planned, hours and issues	Written template by e-mail	Every Friday, 4:00 pm	Each member to the PM	Each member
Milestone report	Report milestone status to the sponsor	Written table (Section 10)	Every second Friday and at each milestone	PM and sponsor	Project Manager
Team group chat	Quick questions, links, day-to-day coordination	Telegram group	Continuous	All members	Project Manager
Source code / document repository	Single source of truth for code and documents	GitHub + shared Drive folder	Continuous	All members	Technical Lead

Change request	Request, assess and approve/reject a change to scope, schedule or cost	Change request form logged in the change log	As needed	Requester, PM, sponsor	Project Manager
----------------	--	--	-----------	------------------------	-----------------

Escalation path: a blocker raised at the stand-up that is not cleared within one working day goes to the project manager; anything affecting scope, the 6-week schedule or the approved budget goes from the project manager to the sponsor through a change request.

2. Project Management Approach

The group applies a hybrid approach. The project as a whole is managed through the five project management process groups – initiating, planning, executing, monitoring and controlling, and closing – exactly as set out in the course and in the JWD Consulting case study. Within the executing process group, the four MVP modules are built incrementally in two iterations, each ending in a working increment that is demonstrated and accepted.

Why this approach fits a 4-module, six-week project:

- A fixed, short deadline and a deliberately narrowed scope. Reducing twelve product characteristics to four modules, as directed, makes a single predictive baseline realistic to hold for the whole six weeks.
- Requirements that will move. Neither shop owners nor customers have used a product like this before, so two iterations still let the group absorb feedback once at the mid-point without reopening the baseline.
- A part-time student team. Each member contributes about 12 hours per week; with only four modules, each iteration can run longer (about a week and a half) than the original one-week cadence, giving more room to build and test properly.
- Lower integration risk than the original twelve-characteristic plan. Four modules built by clearly paired owners integrate through two checkpoints instead of three, and continuous integration from day one of executing keeps that risk small.

How the process groups map onto the six weeks

Process group	Weeks	Main activities and outputs
Initiating	Week 1 (days 1–4)	Identify stakeholders, confirm roles, develop the business case, draft and sign the project charter, hold the kick-off meeting.
Planning	Weeks 1–2 (days 5–10)	Sign the team charter, elicit and analyse requirements, prepare the scope statement (4 MVP modules), create the WBS and WBS dictionary, build the schedule and cost baseline, identify and prioritise risks.
Executing	Weeks 3–6 (days 11–29)	Set up environments and CI/CD, produce the UI/UX design and architecture, then deliver Iteration 1 (Module A + B) and Iteration 2 (Module C + D), integration and regression testing, user acceptance testing, training material, production deployment and pilot roll-out.
Monitoring and Controlling	Weeks 1–6 (days 1–30)	Weekly progress reports every Friday, tracking of schedule, scope and cost against the baseline, change control, and continuous update of the risk register.
Closing	Week 6 (days 28–30)	Final project report, final presentation and product demonstration, sponsor acceptance sign-off, lessons-learned report and document archiving.

Monitoring and controlling runs across the whole project rather than in a phase of its own, which is why it appears in the Gantt chart as three continuous 30-day tasks.

3. Business Case

3.1 Introduction / background

Retail trade in Addis Ababa is dominated by small and medium shops that sell face to face. A shop owner who wants to reach customers beyond the people who walk past the door has few options: a social-media page with no catalogue, no stock information and no payment; or a national e-commerce platform whose joining fees and delivery model are built for larger sellers. Customers, for their part, travel from shop to shop to find an item and compare prices.

The group proposes to build AddisSuq, a hyper-local marketplace. For this six-week course project the instructor has asked the group to implement three to four modules rather than the full product; the group has chosen the four that together deliver one real, testable order: a shop can be found and can sell, and a customer can discover, buy, pay and receive.

3.2 Business objective

- give small and medium retail shops a low-cost digital sales channel that they can operate from a phone;
- reduce the time and transport cost a customer spends finding and buying everyday goods nearby;
- prove, within six weeks, a complete order-to-delivery flow that can be extended with ratings, vendor reporting and a full admin console in a later phase;
- build a base of onboarded shops and repeat customers in one sub-city that can be replicated after the pilot.

3.3 Current situation and problem / opportunity statement

Today a shop owner has no catalogue online, no way to show live stock, and no way to accept an order and a payment remotely. A customer has no way to search what nearby shops hold. The opportunity is to occupy that gap with a product that is cheap for a shop to join and obviously useful to a customer within walking or short driving distance and, within a six-week course project, to prove the core of that flow end to end rather than build every feature shallowly.

3.4 Critical assumptions and constraints

- Merchant payment accounts. Telebirr, CBE Birr and Chapa merchant and sandbox credentials must be obtained early; the design must work with a mock payment service until they arrive, and cash on delivery must always remain available.
- Vendor participation. Onboarding support, free listing and zero commission during the pilot are required, not optional.
- Team capacity. Eight part-time student members contributing about 12 hours per week each, about 594 person-hours, within a fixed six-week window.
- Fixed budget. The project must be delivered for no more than ETB 225,000 including a contingency reserve.
- Reduced scope by instructor direction. Only Modules A–D (Section 1.2) are built; ratings/reviews, the vendor dashboard and the full admin console are explicitly out of scope for this project (Section 6.2) and do not consume schedule or budget.

3.5 Analysis of options and recommendation

Option	Description	Assessment
1. Do nothing	Shops continue to sell only to walk-in customers and through social-media pages.	No cost, but no benefit and the course project objective is not met. Rejected.
2. Social-media selling with an order form	Help shops sell through existing social pages with a shared order form and manual coordination.	Cheap and quick, but no catalogue, no distance search, no integrated payment, no order tracking. Rejected.
3. Join an existing national platform	Onboard local shops onto an existing e-commerce platform.	Avoids development entirely, but the group controls neither commission nor delivery model, and no product is produced for the course. Rejected.
4. Build a 4-module MVP of the hyper-local marketplace (recommended)	Build vendor onboarding & catalogue, customer accounts & discovery, cart/checkout/payment, and delivery/tracking deferring ratings, dashboard and admin console.	Highest cost of the four, but the only one that proves a real order-to-delivery flow within six weeks. Financially attractive: NPV of ETB 819,481 and payback within the first year once the full product is completed. Recommended.

Recommendation: proceed with Option 4, scoped to the four MVP modules. The six-week pilot limits exposure: if the pilot does not attract shops and orders, the loss is bounded by the ETB 225,000 already committed.

3.6 Preliminary project requirements (MVP)

- vendor onboarding with trade licence and TIN upload and administrator approval, plus a product catalogue with categories, photos, prices and live inventory (Module A);
- customer accounts with phone verification and location capture, plus location-based product discovery with filters and keyword search (Module B);
- a shopping cart, order placement, and integration with Telebirr, CBE Birr, Chapa and cash on delivery (Module C);
- same-day delivery, scheduled delivery or in-store pickup, and order-status tracking with SMS/e-mail notification (Module D);
- baseline security, performance and bilingual (Amharic/English) requirements applied across all four modules (Section 6.3).

3.7 Budget estimate and financial analysis

The project is estimated at ETB 225,000. The team size and six-week duration are unchanged from the full-scope plan the same eight members work the same weeks so labour cost is unchanged; the narrower module count is realised as extra schedule float and lower integration risk (Sections 7–9) rather than a smaller budget. Section 11 gives the line-by-line cost baseline.

Operating cost after launch is estimated at ETB 180,000 per year. Benefits are the 5% commission on an estimated ETB 12,000,000 of annual transaction value once the full product (including the deferred modules) is in operation, that is ETB 600,000 per year. Exhibit A shows the discounted cash flow at a 10% discount rate; it is unchanged from the full-scope business case because it values the platform once complete, not the six-week MVP alone.

Exhibit A financial analysis (ETB)	Year 0	Year 1	Year 2	Year 3
Discount rate	10%			
Costs	225,000	180,000	180,000	180,000
Discount factor	1.0000	0.9091	0.8264	0.7513
Discounted costs	225,000	163,636	148,760	135,235
Benefits	0	600,000	600,000	600,000
Discounted benefits	0	545,455	495,868	450,789
Cumulative discounted benefits – costs	(225,000)	156,818	503,925	819,479

Net present value (NPV): ETB 819,481. Discounted life-cycle ROI: 122%. Payback period: Year 1.

3.8 Schedule estimate

The sponsor requires the four-module MVP within six weeks. The group estimates the project can be completed in 30 working days, from Mon 20 Jul to Fri 28 Aug, with the final presentation, acceptance sign-off and lessons-learned report on the last day and submission of all documents by 30 August 2026.

3.9 Potential risks

The main risks are low vendor sign-up, delay in obtaining payment gateway approval, competing coursework reducing team availability, security of customer and payment data, and pressure to add back the deferred features (scope creep). Section 9 gives the full prioritised risk register with the planned response to each risk.

4. Project Charter

Project title	Retail & Local E-Commerce 4-module MVP
Product name	AddisSuq hyper-local retail marketplace
Project start date	Mon 20 Jul 2026

Projected finish date	Fri 28 Aug 2026
Course	Software Project Management (SE341), Group 3
Budget information	Estimated budget ETB 225,000 (assumed estimate): ETB 209,500 direct estimate for labour, hosting, gateway and SMS charges, design tooling and test devices, and ETB 15,500 contingency reserve ($\approx 7.5\%$). Total estimated effort 594 person-hours. Full baseline in Section 11.
Project manager	Yared Mengiste (ZP9157), reachable through the group Telegram channel and institutional e-mail
Project sponsor	Mr. Hassen Redwan, Course Instructor, acting as sponsor and client representative

Project objectives

Design, build and pilot the AddisSuq MVP: a web and mobile hyper-local marketplace covering four modules – vendor onboarding and product catalogue; customer accounts, location and discovery; shopping cart, checkout and payment; and delivery/pickup, order tracking and notification. Per the instructor's direction to scope the six-week build to three or four modules, ratings/reviews, the vendor dashboard and the full admin console are deferred beyond this project. The project must be completed within six weeks, from Mon 20 Jul to Fri 28 Aug, for no more than ETB 225,000.

Specific objectives:

- implement the four MVP modules and their requirements listed in the scope statement (Section 6.3);
- deliver the software in two iterations, each ending in an accepted working increment;
- run user acceptance testing with real pilot shops and customers before deployment;
- deploy the pilot to production and roll it out with at least five onboarded shops;
- produce and submit the business case, project charter, team charter, scope statement, WBS, schedule and Gantt chart, cost baseline, risk register, milestone reports, final project report and lessons-learned report by 30 August 2026.

Main project success criterion

The project will be considered successful if, by Fri 28 Aug, the MVP pilot platform is deployed and in use, with at least five onboarded shops offering at least 100 listed products, and at least 25 end-to-end customer orders – including at least eight paid through an online payment gateway – completed from placement to delivery or collection, with the sponsor's written acceptance sign-off obtained and all required documents submitted.

Secondary criteria: delivery within the six-week schedule and within the ETB 225,000 budget; all four MVP modules implemented and passing user acceptance testing with no open high or critical defects and no more than three open medium defects. The sponsor has agreed that a small schedule or cost overrun would still be acceptable provided the pilot demonstrates a working end-to-end order-to-delivery flow with real local shops.

Approach

- manage the project through the five project management process groups and control it against a single baseline schedule and cost estimate;
- elicit requirements through a customer survey and shop-owner interviews in the first two weeks, and baseline the scope statement, WBS, schedule and cost before any construction begins;
- build the software in two iterations – (1) Module A + Module B, (2) Module C + Module D – demonstrating and obtaining acceptance of each increment;
- set up continuous integration and a test environment on the first day of executing and integrate at every iteration review;
- build the payment integration behind an interface with a mock payment service, so late arrival of merchant credentials does not stop development;
- hold a 15-minute daily stand-up, submit a written weekly progress report every Friday, and report milestone status to the sponsor fortnightly;
- process any change to scope, schedule or cost – including any request to add back a deferred module – through a written change request approved by the project manager and the sponsor;
- close the project with a final report, a product demonstration, sponsor acceptance sign-off and a lessons-learned report.

Sign-off

By signing below, each member confirms that they have read this charter, accept the role and responsibilities assigned to them, and commit approximately 12 hours per week to the project for its six-week duration.

Name	ID	Role	Signature	Date
Mr. Hassen Redwan		Project Sponsor		
Yared Mengiste	ZP9157	Project Manager		
Abenezer Yohannes	PJ4151	Business Analyst		
Nathnael Mesfin	OT8453	Technical Lead		
Osama Sufiyan	YT1430	Backend Developer		
Saron Edosa	ZZ9284	UI/UX Designer		
Yasser Abdulhafiz	KE2168	Frontend Developer		
Yamlak Abnet	AI0828	Frontend Developer		
Zikra Seid	BB1717	QA / Risk Officer		

Comments from stakeholders

Mr. Hassen Redwan (Sponsor)	<i>"Four modules is the right size for six weeks. I want to see one complete, real order placed, paid and delivered by the second iteration review, not only at the final demonstration."</i>
Yared Mengiste (Project Manager)	<i>"Payment gateway credentials are the one thing outside our control. We are applying in week 1 and building against a mock payment service so a delay cannot stop the iteration."</i>
Pilot shop owner (Merkato area boutique)	<i>"I will list my products if someone helps me photograph them and there is no joining fee. My customers pay with Telebirr or cash, so both must work."</i>

5. Team Charter

Project name	Retail & Local E-Commerce 4-module MVP
Team	Group 3, Software Project Management (SE341)
Date agreed	Fri 24 Jul 2026

Code of conduct as a project team we will:

- treat every member's opinion, code and design work with respect, and criticise the work rather than the person;
- be honest about progress a task that is behind is reported at the next stand-up, not hidden until the deadline;
- keep commitments; if a member cannot deliver, they say so early so the work can be reassigned;
- keep customer, shop-owner and test data confidential and use it only for the project.

Participation we will:

- each contribute approximately 12 hours per week for the six weeks of the project;
- attend the daily 15-minute stand-up, or send written status beforehand if genuinely unable to attend;
- attend both iteration planning meetings and both iteration reviews;
- submit an individual weekly progress report to the project manager every Friday by 4:00 pm;
- review one another's work every module has a named reviewer as well as a named builder.

Communication we will:

- use the group Telegram channel for day-to-day coordination and expect a reply within four hours during the day;
- keep all code in the shared GitHub repository and all documents in the shared drive folder;

- push code at least once a day so that work in progress is visible.

Problem solving we will:

- raise a technical blocker at the stand-up on the day it appears, and escalate anything not cleared within one working day to the project manager;
- decide by discussion, and where discussion does not converge, by majority vote with the project manager holding the deciding vote on a tie;
- take any change affecting scope (including requests to add back a deferred module), schedule or budget to the sponsor through a written change request.

Meeting guidelines we will:

- hold the stand-up at 5:00 pm every working day and keep it to 15 minutes;
- hold iteration planning on the first working day of each of the 2 iterations and the review on its last working day;
- close every meeting by restating who owns which action and by when.

6. Project Scope Statement

Project title	Retail & Local E-Commerce 4-module MVP
Date	Thu 30 Jul 2026 (approved by the sponsor)
Prepared by	Abenezer Yohannes (PJ4151), Requirements / Business Analyst, reviewed by Yared Mengiste (ZP9157), Project Manager
Course	Software Project Management (SE341), Group 3

6.1 Project summary and justification

Small and medium retail shops in Addis Ababa sell almost entirely to walk-in customers, with no affordable way to publish a catalogue or take a remote order and payment. The instructor has directed the group to implement three to four modules within the six-week window rather than the full twelve-characteristic product described in the original business case. The group selected four modules Vendor Onboarding & Product Catalogue, Customer Accounts/Location/Discovery, Cart/Checkout/Payment, and Delivery/Tracking/Notifications because together they are the smallest set that lets a real customer complete a real, trackable order from a real shop.

The investment is justified in the business case in Section 3: at an estimated ETB 12,000,000 of annual transaction value and a 5% commission once the full product is complete, the discounted cash flow gives a net present value of ETB 819,481. This six-week project delivers the working MVP and the complete set of project management documents required by the course.

6.2 Scope boundaries

In scope:

- the four MVP modules: (A) vendor onboarding and product catalogue, (B) customer accounts, location capture and location-based discovery, (C) shopping cart, order placement and payment, (D) delivery/pickup scheduling, order tracking and notifications;
- the customer web and mobile interface and the vendor interface needed to operate those four modules;
- integration with the Telebirr, CBE Birr and Chapa payment gateways, cash on delivery, and an SMS gateway;
- a pilot roll-out in one or two sub-cities of Addis Ababa with at least five shops;
- vendor and customer documentation and vendor training material for the four modules.

Out of scope for this project:

- ratings and reviews (deferred originally product characteristic 9);
- the vendor sales dashboard and reports (deferred originally product characteristic 10);
- the full platform administration console beyond the minimal vendor-approval action needed by Module A (deferred originally product characteristic 11);
- a native iOS application the pilot targets the web and Android;

- a rider mobile application with live GPS tracking; delivery handover is confirmed manually in the pilot;
- warehouse or fulfilment-centre operations, credit/instalment payment or a platform wallet;
- expansion beyond Addis Ababa, and any language other than Amharic and English;
- integration with vendors' existing accounting or point-of-sale systems.

Any request to bring a deferred item back into scope is treated as a change request under Section 1.4 and must be approved by the project manager and the sponsor; the schedule and budget in this document assume none are approved.

6.3 Product characteristics and requirements (4 MVP modules)

No.	Module	Requirements
A	Vendor onboarding & product catalogue	A shop owner registers with shop name, owner name, phone, sub-city, address with a map pin, trading hours and category, and uploads a trade licence and TIN certificate; an administrator approves or rejects the application. A vendor then creates, edits, publishes and unpublishes products with bilingual names, category, description, price, up to five photos and quantity; stock decrements on a confirmed order and a product hides automatically at zero stock. Target: registration completed in under 15 minutes from a phone; catalogue holds at least 1,000 products at pilot launch.
B	Customer accounts, location & discovery	A customer signs up with a phone number verified by a one-time password and maintains a profile with up to three saved addresses. Current location is captured from the device or entered manually. Products and shops are listed ranked by distance, with filters for sub-city, category and price, and bilingual keyword search. Target: search returns results in under three seconds for 95% of queries.
C	Shopping cart, checkout & payment	A customer adds products to a cart (one cart per shop), places the order, and chooses delivery or pickup and a payment method. The platform accepts Telebirr, CBE Birr and Chapa for online payment and cash on delivery; all payment traffic uses HTTPS/TLS 1.2+ and no card data is stored on platform servers. An order confirmation is issued within ten seconds and the vendor is notified immediately; a failed or abandoned payment expires after 30 minutes and releases reserved stock.
D	Delivery/pickup, order tracking & notifications	A customer chooses same-day delivery within a 7 km radius, scheduled delivery, or in-store pickup, with a distance-band delivery fee. An order moves through Placed, Confirmed, Packed, Out for delivery/Ready for collection, and Delivered/Collected, or Cancelled with a reason. The customer and vendor receive an SMS and e-mail at every status change, and the customer can see the current state in the app.

Baseline non-functional requirements applied across all four modules: role-based access for the customer, vendor and administrator roles; passwords stored only as salted hashes; one-time passwords expiring after five minutes; support for 300 concurrent pilot users with page response under three seconds; support for current Chrome, Firefox and Edge and Android 9 and above; the interface available in Amharic and English.

6.4 Project-management-related deliverables

Deliverable	Description
Business case	Justification for the investment, options analysis and the discounted cash flow in Exhibit A.
Project charter	Signed authorisation with objectives, success criterion, approach, budget and roles.
Team charter	Agreed code of conduct, participation, communication, problem solving and meeting guidelines.
Project scope statement	This document the four MVP modules, deliverables and success criteria.
WBS and WBS dictionary	Deliverable-oriented decomposition to work-package level.
Project schedule and Gantt chart	Baseline schedule with durations, dates, dependencies, milestones and the critical path.

Cost baseline	Line-by-line cost estimate of ETB 225,000 including the contingency reserve.
Prioritised risk register	Ranked risks with probability, impact and the planned response.
Weekly progress reports & milestone reports	Recorded work, hours and issues; milestone status reported to the sponsor.
Change request log	Every requested change including any request to add a deferred module with its decision.
Final project report, presentation & lessons-learned report	Complete record of the project against its success criteria, live demonstration, and reflection.

6.5 Product-related deliverables

Deliverable	Description
Requirements survey and results	Customer survey instrument, shop-owner interview guide and the analysed responses.
Software requirements specification	Functional and non-functional requirements with use cases for the four MVP modules.
UI/UX design package	Wireframes, style guide and key screens for Modules A–D in Amharic and English.
Architecture and data design	Architecture document, entity-relationship diagram and API contract specification.
Iteration 1 increment	Working vendor onboarding, shop profiles and product catalogue (Module A); customer accounts, location capture and location-based search (Module B).
Iteration 2 increment	Working shopping cart, checkout and payment gateway integration (Module C); delivery/pickup scheduling and order tracking with notifications (Module D).
Source code repository with CI/CD	Version-controlled source code with the build, test and deployment pipeline.
Test plan, test cases and test reports	Unit and integration test cases, regression suite, defect log and test summary.
Deployed pilot platform	The four-module MVP running on cloud hosting with a registered domain and SSL.
User documentation	Vendor onboarding guide and customer help pages for the four modules.
Promotion and launch package	Launch promotion material, shop signage and social media content for the pilot.
Deployment and transition handover	Deployment runbook, configuration inventory and support handover notes.

6.6 Project success criteria

- The project is completed within the six-week window, Mon 20 Jul to Fri 28 Aug, and for no more than ETB 225,000 including the contingency reserve.
- All four MVP modules listed in Section 6.3 are implemented and pass user acceptance testing, with zero open high or critical defects and no more than three open medium defects at deployment.
- The pilot is launched with at least five onboarded and approved shops offering at least 100 listed products.
- At least 15 test customers complete at least 25 end-to-end orders, of which at least eight are paid through an online payment gateway, from placement to delivery or collection.
- Keyword search returns results in under three seconds for 95% of queries.
- The sponsor's written acceptance sign-off is obtained and all project management and product deliverables are submitted by 30 August 2026.

The sponsor has stated that a small overrun of the schedule or the budget would still leave the project successful, provided the pilot demonstrates a working end-to-end order-to-delivery flow with real local shops and real customers.

7. Work Breakdown Structure (WBS)

The WBS is derived directly from the scope statement in Section 6 and is organised by the five project management process groups at level 1. Level 2 holds the deliverables of each process group, and level 3 the work packages that produce them. Only the work listed here is in scope; the deferred features in Section 6.2 are not in the WBS.

7.1 WBS in outline form

1.0 Initiating

- 1.1 Identify stakeholders and confirm team roles
- 1.2 Develop the business case
- 1.3 Draft and sign the project charter
- 1.4 Hold the project kick-off meeting

2.0 Planning

- 2.1 Hold team planning meeting and sign the team charter
- 2.2 Elicit and analyse requirements
 - 2.2.1 Design and run the customer survey
 - 2.2.2 Interview shop owners
 - 2.2.3 Analyse results and write the requirements specification
- 2.3 Prepare the project scope statement (4 MVP modules)
- 2.4 Create the WBS and WBS dictionary
- 2.5 Develop the schedule and cost baseline
 - 2.5.1 Estimate task resources and durations
 - 2.5.2 Determine task dependencies and draft the Gantt chart
 - 2.5.3 Prepare and baseline the cost estimate
- 2.6 Identify and prioritise project risks
- 2.7 ♦ Planning documents approved (milestone)

3.0 Executing

- 3.1 Set up development and test environments and the CI/CD pipeline
- 3.2 Produce the UI/UX design (wireframes, style guide, key screens)
- 3.3 Define the system architecture, data model and API contracts
- 3.4 Iteration 1 Module A (Vendor onboarding & catalogue) + Module B (Customer accounts & discovery)
 - 3.4.1 Build vendor registration, shop profile and admin approval (Module A)
 - 3.4.2 Build the product catalogue, categories and inventory management (Module A)
 - 3.4.3 Build customer sign-up, log-in and location capture (Module B)
 - 3.4.4 Build location-based product search and browsing (Module B)
 - 3.4.5 ♦ Iteration 1 increment accepted (milestone)
- 3.5 Iteration 2 Module C (Cart, checkout, payment) + Module D (Delivery, tracking, notifications)
 - 3.5.1 Build the shopping cart and order placement (Module C)
 - 3.5.2 Integrate payment gateways and cash on delivery (Module C)
 - 3.5.3 Build delivery/pickup scheduling and delivery-fee calculation (Module D)
 - 3.5.4 Build order tracking and the notification service (Module D)
 - 3.5.5 ♦ Iteration 2 increment accepted (milestone)
- 3.6 Carry out system integration and regression testing
- 3.7 Run user acceptance testing with pilot shops and customers
- 3.8 Prepare vendor training material, user guide and launch promotion
- 3.9 Deploy to production and roll out the pilot launch
- 3.10 ♦ Software product delivered (milestone)

4.0 Monitoring and Controlling

- 4.1 Submit weekly progress reports

4.2 Track schedule, scope and cost; process change requests

4.3 Update the risk register and take corrective action

5.0 Closing

5.1 Prepare the final project report

5.2 Deliver the final project presentation and product demonstration

5.3 ♦ Sponsor / client acceptance sign-off obtained (milestone)

5.4 Submit the lessons-learned report and archive project documents

Levels 1 to 3 above are the WBS proper. Items marked (milestone) are zero-duration checkpoints used to control the schedule rather than work packages.

7.2 WBS dictionary (selected work packages)

The dictionary records what each work package includes and how the team will know it is finished. The packages below carry the most technical risk or the most scope; the remaining packages are described in the full dictionary held in the project repository.

WBS	Work package	Owner	Description and completion criteria	Duration
2.2	Elicit and analyse requirements	Abenezer	Run a customer survey, interview shop owners, and turn responses into functional/non-functional requirements for the 4 MVP modules. Complete when the team reviews the requirements specification.	3 days
2.3	Prepare the scope statement	Abenezer	Define scope boundaries, the four module requirements and success criteria. Complete when the sponsor approves the scope statement.	2 days
3.1	Set up environments and CI/CD	Nathnael	Provision dev/test/production environments and the build-test-deploy pipeline. Complete when a commit automatically builds, tests and deploys.	2 days
3.3	Architecture, data model & API contracts	Nathnael	Define the architecture, entity-relationship model and REST API contracts the four modules build against. Complete when the team accepts the contracts.	2 days
3.4.1	Vendor registration, shop profile & approval	Nathnael	Registration form, document upload and admin approval workflow (Module A). Complete when a shop can register, be approved and get a public profile.	3 days
3.4.2	Product catalogue, categories & inventory	Osama	Vendor product create/edit/publish/unpublish with bilingual names, photos, quantities; stock decrement and auto-hide at zero (Module A). Complete when catalogue test cases pass.	3 days
3.4.4	Location-based search & browsing	Yamlak	Distance-ranked product/shop listing with filters and bilingual keyword search under 3 seconds for 95% of queries (Module B). Complete when search test cases pass.	3 days
3.5.1	Shopping cart & order placement	Osama	Per-shop cart, quantity adjustment and order placement with confirmation within 10 seconds (Module C). Complete when checkout test cases pass.	3 days
3.5.2	Payment gateway integration	Nathnael	Telebirr, CBE Birr and Chapa behind a payment interface, plus cash on delivery, pending-order expiry (Module C). Complete when a sandbox payment succeeds end to end and cash on delivery is confirmed.	4 days
3.5.3 / 3.5.4	Delivery scheduling & order tracking/notifications	Yasser / Yamlak	Delivery/pickup scheduling with fee calculation, and order-status tracking with SMS/e-mail notification at every state change (Module D). Complete when the state machine and notification test cases pass.	2 days each
3.6	System integration and regression testing	Zikra	Integrate the two increments, run the full regression suite, log and triage defects. Complete when no high or critical defect is open.	2 days
3.7	User acceptance testing	Zikra	Five pilot shops and 15 test customers execute the acceptance test scenarios. Complete when the sponsor signs the UAT report.	2 days

3.9	Production deployment and pilot roll-out	Nathnael	Deploy the accepted build to production with domain and SSL, load pilot shops and products, confirm a live end-to-end order. Complete when the pilot is open to customers.	1 day
-----	--	----------	--	-------

8. Project Schedule and Gantt Chart

Project name	Retail & Local E-Commerce 4-module MVP
Project start date	Mon 20 Jul 2026 (working day 1)
Project finish date	Fri 28 Aug 2026 (working day 30)
Duration	6 weeks, 30 working days, Monday to Friday
Baseline approved	Fri 31 Jul 2026, milestone 2.7

8.1 Task list with durations, dates and dependencies

Tasks are grouped under the five project management process groups. Durations are in working days; weekends are non-working. A duration of 0 days denotes a milestone. Predecessors use finish-to-start logic unless marked SS (start-to-start), with any lag given in days.

WBS	Task name	Duration	Start	Finish	Predecessors	Responsible
1.0	Initiating	4 days	20-Jul	23-Jul		Yared
1.1	Identify stakeholders and confirm team roles	1 day	20-Jul	20-Jul		Yared
1.2	Develop the business case	1 day	21-Jul	21-Jul	1.1	Abenezer
1.3	Draft and sign the project charter	1 day	22-Jul	22-Jul	1.2	Yared
1.4	Hold the project kick-off meeting	1 day	23-Jul	23-Jul	1.3	Yared
2.0	Planning	6 days	24-Jul	31-Jul		Yared
2.1	Hold team planning meeting and sign the team charter	1 day	24-Jul	24-Jul	1.4	Yared
2.2	Elicit and analyse requirements (survey, interviews)	3 days	24-Jul	28-Jul	1.4	Abenezer
2.3	Prepare the project scope statement (4 modules)	2 days	29-Jul	30-Jul	2.2	Abenezer
2.4	Create the WBS and WBS dictionary	1 day	30-Jul	30-Jul	2.3 SS+1d	Yared
2.5	<i>Develop the schedule and cost baseline</i>	2 days	30-Jul	31-Jul		Yared
2.5.1	Estimate task resources and durations	1 day	30-Jul	30-Jul	2.4 SS	Yared
2.5.2	Determine dependencies and draft the Gantt chart	1 day	31-Jul	31-Jul	2.5.1	Yared
2.5.3	Prepare and baseline the cost estimate	1 day	31-Jul	31-Jul	2.5.1	Osama
2.6	Identify and prioritise project risks	1 day	31-Jul	31-Jul	2.3	Zikra
2.7	◆ Planning documents approved	0 days	31-Jul	31-Jul	2.4, 2.5, 2.6	Sponsor
3.0	Executing	19 days	03-Aug	27-Aug		Nathnael
3.1	Set up dev/test environments and CI/CD pipeline	2 days	03-Aug	04-Aug	2.7	Nathnael
3.2	Produce the UI/UX design	2 days	03-Aug	04-Aug	2.7	Saron


3.3	Define architecture, data model and API contracts	2 days	03-Aug	04-Aug	2.7	Nathnael
3.4	<i>Iteration 1 Module A + Module B</i>	7 days	05-Aug	13-Aug		All
3.4.1	Build vendor registration, shop profile & approval (A)	3 days	05-Aug	07-Aug	3.1, 3.3	Nathnael
3.4.2	Build the product catalogue & inventory (A)	3 days	05-Aug	07-Aug	3.3	Osama
3.4.3	Build customer sign-up, log-in & location capture (B)	2 days	05-Aug	06-Aug	3.1, 3.2	Yasser
3.4.4	Build location-based search & browsing (B)	3 days	10-Aug	12-Aug	3.4.2	Yamlak
3.4.5	◆ Iteration 1 increment accepted	0 days	13-Aug	13-Aug	3.4.1, 3.4.3, 3.4.4	All
3.5	<i>Iteration 2 Module C + Module D</i>	6 days	14-Aug	21-Aug		All
3.5.1	Build the shopping cart & order placement (C)	3 days	14-Aug	18-Aug	3.4.5	Osama
3.5.2	Integrate payment gateways & cash on delivery (C)	4 days	14-Aug	19-Aug	3.4.5	Nathnael
3.5.3	Build delivery/pickup scheduling & fee calc. (D)	2 days	19-Aug	20-Aug	3.5.1	Yasser
3.5.4	Build order tracking & notification service (D)	2 days	19-Aug	20-Aug	3.5.1	Yamlak
3.5.5	◆ Iteration 2 increment accepted	0 days	21-Aug	21-Aug	3.5.2, 3.5.3, 3.5.4	All
3.6	Carry out system integration & regression testing	2 days	24-Aug	25-Aug	3.5.5	Zikra
3.7	Run user acceptance testing with pilot shops/customers	2 days	25-Aug	26-Aug	3.6 SS+1d	Zikra
3.8	Prepare vendor training material, guide & promotion	2 days	24-Aug	25-Aug	3.5.5	Saron
3.9	Deploy to production and roll out the pilot launch	1 day	27-Aug	27-Aug	3.7, 3.8	Nathnael
3.10	◆ Software product delivered	0 days	27-Aug	27-Aug	3.9	Yared
4.0	Monitoring and Controlling	30 days	20-Jul	28-Aug		Yared
4.1	Submit weekly progress reports (every Friday)	30 days	20-Jul	28-Aug		All
4.2	Track schedule, scope and cost; process change requests	30 days	20-Jul	28-Aug		Yared
4.3	Update the risk register and take corrective action	30 days	20-Jul	28-Aug		Zikra
5.0	Closing	3 days	26-Aug	28-Aug		Yared
5.1	Prepare the final project report	2 days	26-Aug	27-Aug	3.7 SS+1d	Yared
5.2	Deliver the final presentation and product demonstration	1 day	28-Aug	28-Aug	3.10, 5.1	All
5.3	◆ Sponsor / client acceptance sign-off obtained	0 days	28-Aug	28-Aug	5.2	Sponsor

5.4	Submit lessons-learned report and archive documents	1 day	28-Aug	28-Aug	5.2 SS	All
-----	---	-------	--------	--------	--------	-----

Task names shown as milestones (◆) are on the critical path decision points. Section 8.3 lists the full critical path.

8.2 Gantt chart

Each column is one working day, grouped by week. A grey bar is a summary task, a blue bar is a work package, a light-blue bar is continuous monitoring and controlling work, and a gold cell marked **◆** is a zero-duration milestone.

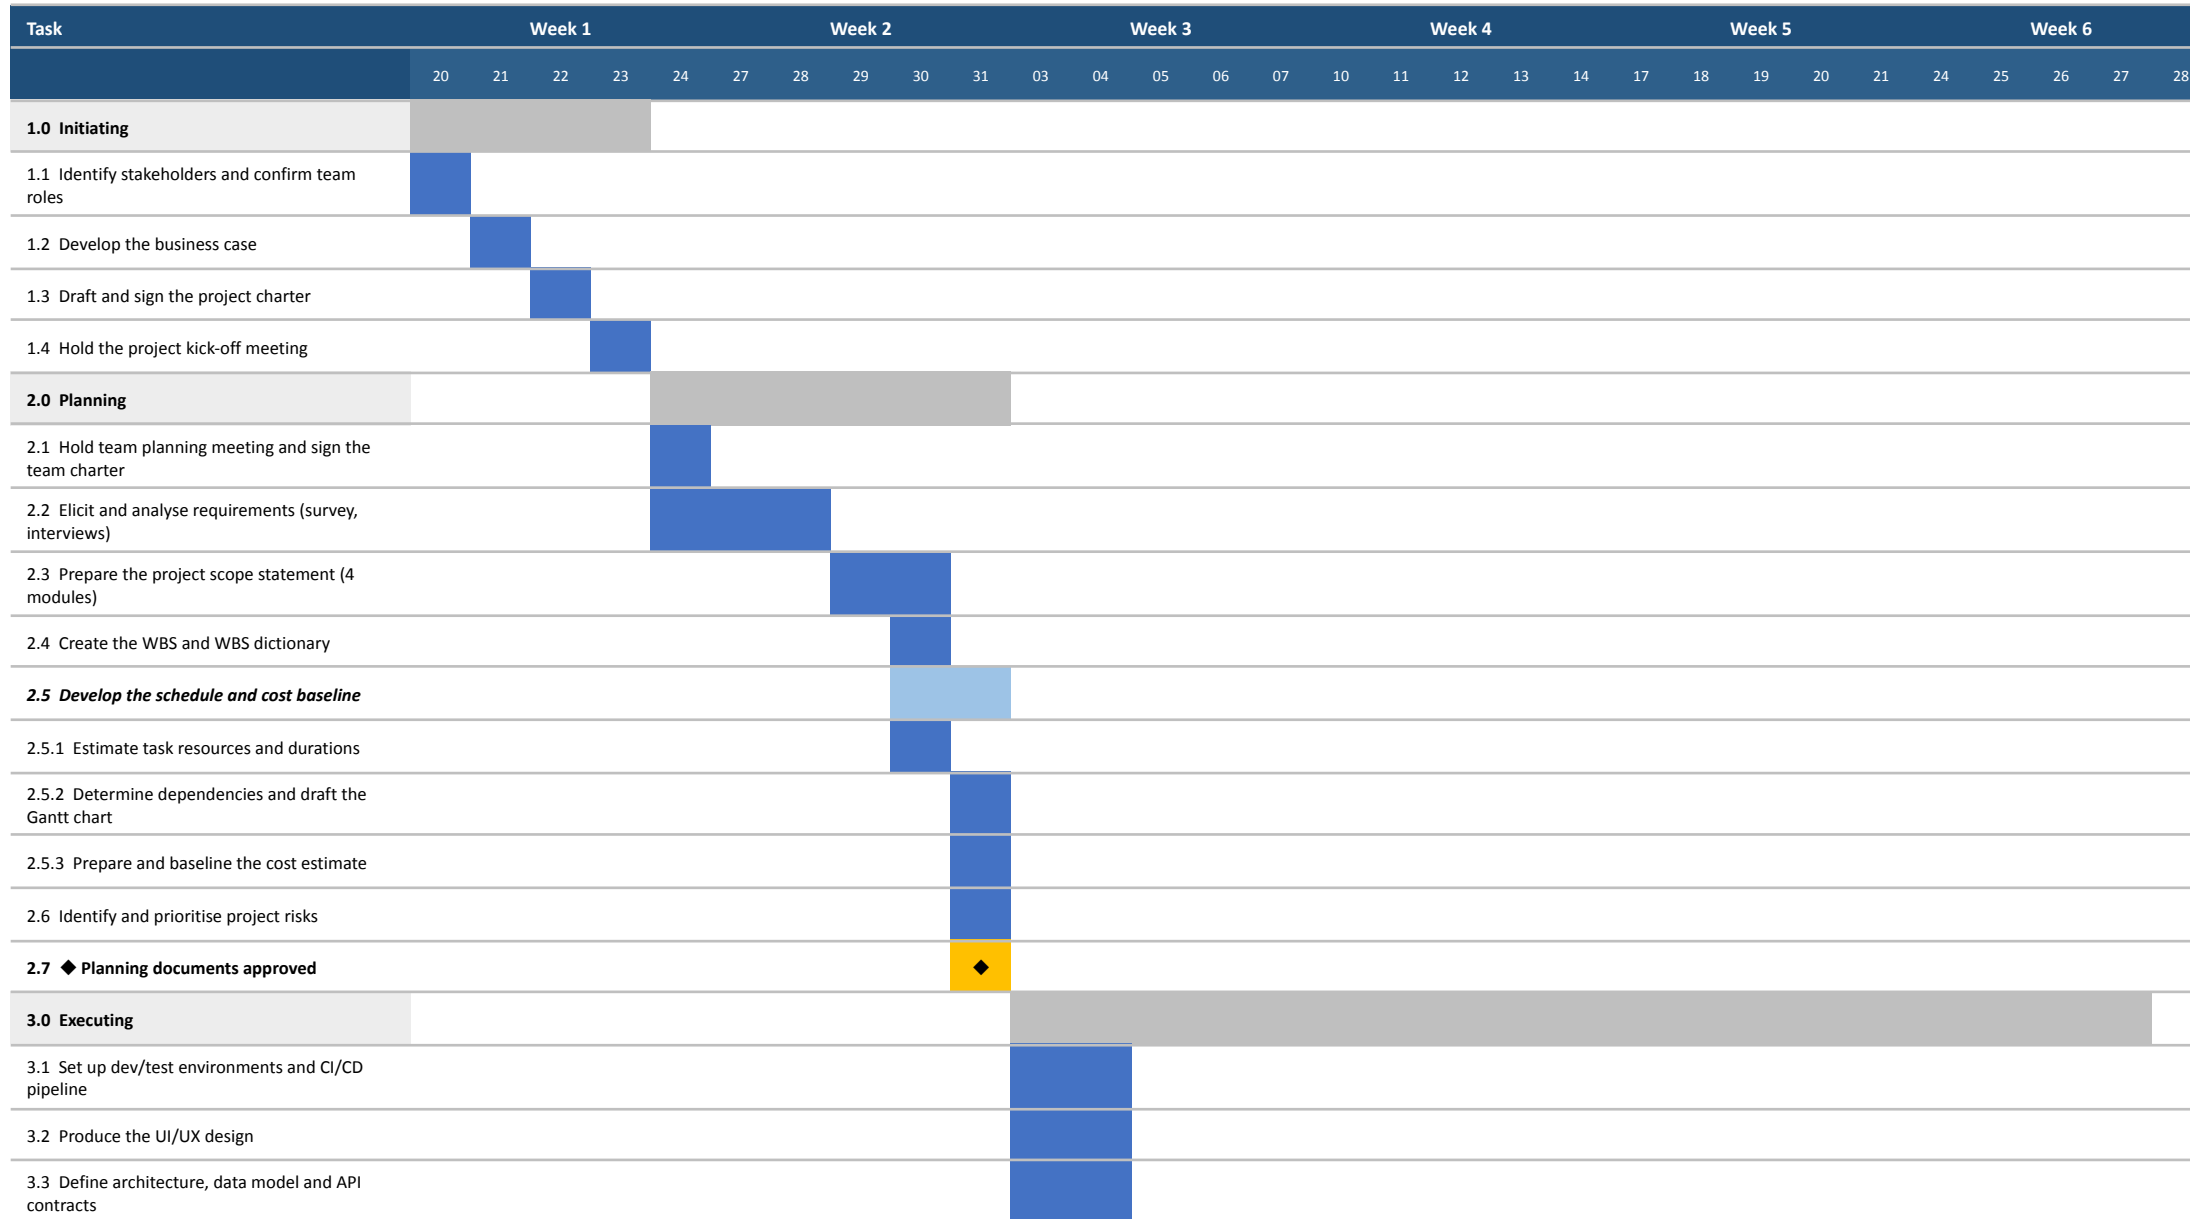



5.2 Deliver the final presentation and product demonstration

5.3 ♦ Sponsor / client acceptance sign-off obtained

5.4 Submit lessons-learned report and archive documents

Legend: ■ Summary ■ Iteration summary ■ Work package ♦ Milestone (0 days)

Notation: predecessors use finish-to-start logic by default. SS means start-to-start; SS+1d means the successor may start one working day after the predecessor starts. Milestones are placed on the day they are confirmed.

8.3 Critical path and schedule notes

Critical path

1.1 → 1.2 → 1.3 → 1.4 → 2.2 → 2.3 → 2.4 → 2.5.1 → 2.5.2 → 2.7 → 3.3 → 3.4.2 → 3.4.4 → 3.4.5 → 3.5.1 → 3.5.3 → 3.5.5 → 3.6 → 3.7 → 3.9 → 3.10 → 5.2

The critical path runs for the full 30 working days with no float. Any slip on one of these tasks slips the project finish date. In words: the path runs from stakeholder identification through the business case, charter and kick-off, into requirements analysis, the scope statement, the WBS, resource and duration estimating and the draft schedule, to baseline approval; then through the architecture into the product catalogue and location-based search of Iteration 1, the cart and the delivery-scheduling work of Iteration 2, and finally integration and regression testing, user acceptance testing, production deployment, product delivery and the final presentation.

Float and overlaps

- 3.5.2 Payment gateway integration carries one working day of float; it is watched closely because merchant credentials are outside the group's control.
- 3.2 UI/UX design and 3.1 environment setup run in parallel with 3.3 architecture in week 3, so construction can start on day 13 for both modules of Iteration 1.
- 2.4 WBS creation starts one day after 2.3 begins (SS+1d) because the WBS is drafted from the first complete draft of the scope statement.
- 3.7 user acceptance testing starts one day after integration testing begins (SS+1d) so pilot shops can start testing accepted modules while regression testing continues.
- 5.1 the final project report starts one day after user acceptance testing begins (SS+1d), so writing overlaps the last test day.
- 4.1 to 4.3, the monitoring and controlling tasks, run for all 30 days and are not on the critical path, but 4.2 change control gates every change that could affect it.

Milestones on the schedule

WBS	Milestone	Date	Working day	Confirms
2.7	Planning documents approved	Fri 31 Jul	Day 10	2.4, 2.5, 2.6
3.4.5	Iteration 1 increment accepted (Modules A + B)	Thu 13 Aug	Day 19	3.4.1, 3.4.3, 3.4.4
3.5.5	Iteration 2 increment accepted (Modules C + D)	Fri 21 Aug	Day 25	3.5.2, 3.5.3, 3.5.4
3.10	Software product delivered	Thu 27 Aug	Day 29	3.9
5.3	Sponsor / client acceptance sign-off obtained	Fri 28 Aug	Day 30	5.2

9. List of Prioritised Risks

Risks were identified in a team brainstorming session during planning (work package 2.6) and are ranked by the combination of probability and impact, most serious first. Zikra Seid owns the register and reviews it with the project manager every Friday.

#	Risk	Prob.	Impact	Planned response
1	Too few shops sign up, so customers find an empty catalogue and do not return	High	High	Recruit five anchor shops before pilot launch; offer free onboarding including product photography; charge zero commission for the whole pilot; assign one team member as the named contact for each pilot shop.
2	Payment gateway merchant approval and sandbox credentials arrive late	High	High	Apply for Telebirr, CBE Birr and Chapa merchant accounts in week 1; build the payment module

				behind an interface against a mock payment service so development does not wait; keep cash on delivery as a working fallback at launch.
3	Team availability falls because of other coursework and examinations	High	Medium	The team charter commits each member to about 12 hours per week; every module has a named builder and reviewer; the schedule keeps float in weeks 5–6 as buffer; the project manager reallocates work at the stand-up as soon as a conflict is reported.
4	Customer personal data or the payment flow is compromised	Medium	High	Store no card data on platform servers; use HTTPS/TLS 1.2+ everywhere; store passwords only as salted hashes; expire one-time passwords after five minutes; include a security review in work package 3.6.
5	Scope creep stakeholders ask for the deferred modules (ratings, dashboard, admin console) to be added back during the pilot	High	Medium	Baseline the scope statement (4 modules) before construction starts; require a written change request approved by the project manager and the sponsor for any change; record other requests in a future-release backlog rather than refusing them outright.
6	Location and distance data are inaccurate, so distance ranking misleads customers	Medium	Medium	Allow landmark-based address entry and a manual map pin in addition to device GPS; fall back to sub-city level ranking when a precise location is unavailable; test distance calculation against known shop locations.
7	No reliable rider network is available for same-day delivery during the pilot	Medium	Medium	Launch with in-store pickup and the shop's own delivery person as the default; contract freelance riders for the pilot area; make delivery-fee bands configurable so pricing can be corrected quickly.
8	The two increments do not integrate cleanly, and integration overruns week 6	Medium	High	Set up continuous integration on the first day of executing (3.1); agree API contracts in 3.3 before construction; integrate and run the regression suite at every iteration review, not only in 3.6.
9	Internet or power interruptions stop work or spoil the final demonstration	Medium	Medium	Keep development environments runnable offline on each member's machine; push code at least once a day; record a full video of the working product before the final demonstration as a backup.
10	Hosting, gateway or SMS charges exceed the estimate	Medium	Low	Hold the ETB 15,500 contingency reserve; monitor spend weekly against the cost baseline; start on the smallest viable hosting tier and buy SMS credits in small batches.
11	Too few pilot customers take part in user acceptance testing	Medium	Medium	Recruit and confirm 15 test customers during week 5; offer a small incentive such as free delivery on the first order; a team member can place test orders on behalf of a customer where a tester drops out.
12	Source code or project documents are lost	Low	High	Keep all code in the shared GitHub remote and all documents in the shared drive; back up the repository and document set to a second cloud drive every week; never leave a deliverable only on one member's laptop.

Risks 1 and 2 are the two the group considers capable of stopping the project from meeting its main success criterion, and both have a response that is already scheduled work: anchor-shop recruitment runs through week 5, and the mock payment service is part of work package 3.5.2. Risk 5 is specific to the reduced-scope decision it is the risk of the module cut not holding.

10. Milestone Report

Project	Retail & Local E-Commerce 4-module MVP (AddisSuq)
Prepared by	Yared Mengiste (ZP9157), Project Manager
Reported to	Mr. Hassen Redwan, Project Sponsor
Report date	Friday 21 August 2026 (end of week 5)
Overall status	On schedule. 15 of 22 milestones/tasks completed, 1 in progress, 3 continuous activities on track, 3 not yet started. No change to the finish date of Friday 28 August 2026.

Milestone	Date	Status	Responsible	Comments
Initiating				
Stakeholders identified and team roles confirmed	Mon 20 Jul	Completed	Yared Mengiste	Sponsor role confirmed with the instructor
Business case approved by the sponsor	Tue 21 Jul	Completed	Abenezer Yohannes	Approved with a request to show the payback year explicitly
Project charter signed by all stakeholders	Wed 22 Jul	Completed	Yared Mengiste	All eight members and the sponsor signed
Project kick-off meeting held	Thu 23 Jul	Completed	Yared Mengiste	All 8 members attended
Planning				
Team charter signed	Fri 24 Jul	Completed	Yared Mengiste	12 hours per week per member agreed
Requirements survey and analysis completed	Tue 28 Jul	Completed	Abenezer Yohannes	38 customer and 10 shop-owner responses collected
Project scope statement approved (4 modules)	Thu 30 Jul	Completed	Abenezer Yohannes	Deferred modules confirmed out of scope with the sponsor
WBS and WBS dictionary completed	Thu 30 Jul	Completed	Yared Mengiste	Reviewed by the whole team
Schedule and cost baseline approved	Fri 31 Jul	Completed	Yared Mengiste	30 working days and ETB 225,000 baselined
Prioritised risk register completed	Fri 31 Jul	Completed	Zikra Seid	12 risks ranked, including the scope-creep risk
Executing				
Development/test environments and CI/CD ready	Tue 4 Aug	Completed	Nathnael Mesfin	Pipeline builds, tests and deploys on every commit
UI/UX design baseline approved	Tue 4 Aug	Completed	Saron Edosa	Key screens for Modules A–D; Amharic labels added
Architecture, data model and API contracts approved	Tue 4 Aug	Completed	Nathnael Mesfin	Contracts frozen before construction started
Iteration 1 increment accepted (Modules A + B)	Thu 13 Aug	Completed	All members	Search response tuned to 2.6 s; catalogue and onboarding demoed live
Iteration 2 increment accepted (Modules C + D)	Fri 21 Aug	In progress	All members	Telebirr sandbox arrived 2 days late; mock payment service kept the team on schedule;

				review closing Mon 24 Aug
System integration and regression testing completed	Tue 25 Aug	Not started	Zikra Seid	Regression suite written during Iteration 2
User acceptance testing signed off	Wed 26 Aug	Not started	Zikra Seid	5 pilot shops and 15 test customers confirmed
Production deployment and pilot roll-out completed	Thu 27 Aug	Not started	Nathnael Mesfin	Domain and SSL certificate already purchased
Software product delivered	Thu 27 Aug	Not started	Yared Mengiste	Milestone 3.10
Monitoring and Controlling				
Weekly progress reports submitted	Every Friday	On track	All members	5 of 5 weekly reports submitted to date
Change requests reviewed and logged	Continuous	On track	Yared Mengiste	2 change requests raised, 1 approved (Amharic labels), 1 deferred (customer wish-list)
Risk register reviewed and updated	Every Friday	On track	Zikra Seid	Risk 2 downgraded after the sandbox credentials arrived
Closing				
Final project report completed	Thu 27 Aug	Not started	Yared Mengiste	Sections 1–8 already drafted
Final presentation and demonstration delivered	Fri 28 Aug	Not started	All members	Backup demonstration video to be recorded 27 Aug
Sponsor acceptance sign-off obtained	Fri 28 Aug	Not started	Sponsor / Yared Mengiste	Against the success criteria in Section 6.6
Lessons-learned report submitted and documents archived	Fri 28 Aug	Not started	All members	Documents to be archived in the shared drive

Notes on the current position

- The only milestone not yet met on its planned date is the Iteration 2 review, moved from Friday 21 to Monday 24 August after the Telebirr sandbox credentials arrived two days late; because the payment module was built against a mock payment service (risk 2 response), no schedule time was lost.
- Two of the two change requests raised so far were resolved: adding Amharic product names to the catalogue was approved; a customer wish-list feature was deferred to a future release rather than added into the six-week baseline.
- Remaining risk attention for week 6 is on user acceptance testing participation (risk 11) and on the production deployment window (risk 9).

11. Cost Baseline and Budget Detail

The budget in the project charter is an assumed estimate prepared during planning (work package 2.5.3) and baselined on 31 July 2026. It is a bottom-up estimate: labour comes from the effort in the schedule, and direct costs from supplier prices obtained during planning. Reducing the scope to four modules does not reduce labour cost, since the same eight members work the same six weeks; it is realised instead as schedule float and lower integration risk (Sections 7–9).

Cost item	Basis of estimate	Amount (ETB)
Project manager labour	90 hours × ETB 350 per hour	31,500

Team member labour (7 members)	504 hours × ETB 250 per hour	126,000
Cloud hosting, domain and SSL certificate	One year, smallest viable tier	18,000
Payment gateway integration and sandbox fees	Telebirr, CBE Birr and Chapa set-up	15,000
SMS and notification gateway credits	Pilot volume	6,000
UI/UX design tool licences	6 weeks, 4 modules	5,000
Test devices, internet and data bundles	Android test handsets and data	8,000
Subtotal direct estimate		209,500
Contingency reserve	Approximately 7.5% of the subtotal	15,500

Effort basis

- the project manager contributes 15 hours per week for 6 weeks, a total of 90 hours;
- each of the other seven members contributes 12 hours per week for 6 weeks, that is 72 hours each and 504 hours in total;
- total project effort is therefore 594 person-hours, about 99 hours per week across the team;
- labour rates are notional student rates agreed with the sponsor for the purpose of this estimate; no cash is paid to members.

Cost control

The project manager compares committed cost against this baseline every Friday as part of work package 4.2. Use of the contingency reserve requires the sponsor's approval through a change request. Operating cost after the pilot, used in the business case, is estimated at ETB 180,000 per year.

12. Conclusion

This report applies the five project management process groups to a deliberately reduced, four-module MVP of the Retail & Local E-Commerce project, as directed by the course instructor. The initiating documents establish why the product is worth building and who is accountable; the planning documents fix what four modules will be delivered, in what order, by when and at what cost; the executing plan delivers the software in two iterations with continuous integration; the monitoring and controlling activities run across all six weeks through weekly reports, baseline tracking, change control and the risk register; and the closing activities end the project with a demonstration, an acceptance sign-off and a lessons-learned report.

The plan is sized for a part-time team of eight working within a fixed six-week window and an assumed budget of ETB 225,000. Its main success criterion is not the completion of documents but a working pilot of the four core modules: five onboarded shops, 100 listed products and 25 end-to-end orders through real local shops by Fri 28 Aug. Ratings and reviews, the vendor dashboard and the full admin console remain a clearly scoped next phase rather than a gap in this project.

References

- Schwalbe, K. Information Technology Project Management the JWD Consulting intranet site case study, used as the model for the document set in this report.
- Software Project Management (SE341) course notes and handouts, HiLCoE School of Computer Science & Technology.
